


## Launch Campaign Newsletter #06 – Friday, 1. June 2018



Wednesday, the container-ship “CMA CGM Brasil” has arrived in Degrad de Cannes (port of Cayenne). 10 sea container, containing BC solar array deployment rig and scaffolding have been unloaded and transferred to CSG on Thursday.

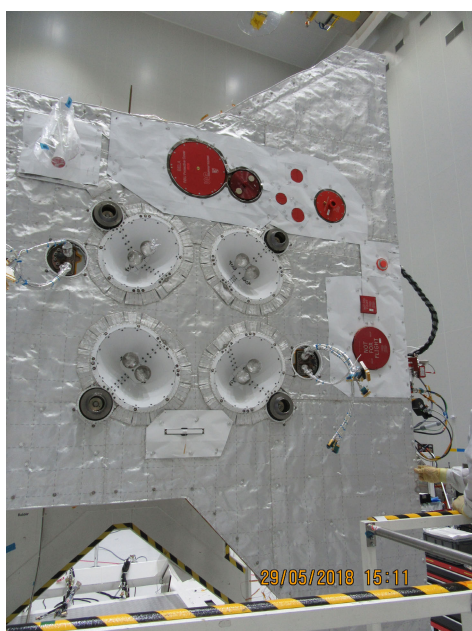

Main activities on MPO during this week has been the installation and sewing of HT (High Temperature) MLI and the nanovation coated titanium foil MLI on the nadir side. In addition, the 22N thruster heat shield has been finalised.

On MTM, the 10N thruster have been cleaned, leak checked and inspected. Setup of MTM and the associated FGSE (Fluidical Ground Support Equipment) has been completed. Sequence of dedicated leak checks has started.

JAXA has completed the MMO RCS (Reaction Control System) leak test, and is ready for the final nitrogen tank pressurisation, planned for next week.

